


Levee Repairs Approved

As of Jul 1, 2020

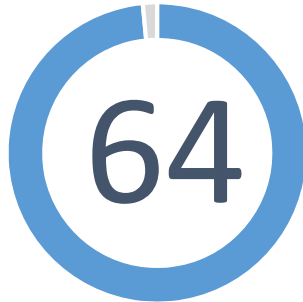

UP ONE

We expect to have repairs approved for a total of 65 levees.

Levee Repair Contracts Awarded

As of Jul 1, 2020



UP ONE

We expect to award a total of 56 levee repair contracts.

Remaining Breached Levees

As of Jul 1, 2020



DOWN TWO

We expect to repair a total of 65 levee segments.

Details on Levee Repairs Approved

See attached table, "Status of Levee Rehabilitation Requests for Assistance"

Repairs are being evaluated for the following levee: L-385

Details on Levee Repair Contracts Awarded

See attached table, "Status of Construction Projects"

37 contracts have been awarded to repair 46 damaged levees

52 out of the expected 65 levee units have been advertised and/or awarded. This leaves 13 Levee Units yet to advertise as follows:

- 10 - NON FEDS: Dewitt 1&2; Holt 9; Holt 10; Mo Valley L & D; Mo Valley 1 & 2; Platte Co Sec 1 / Rushville Sugarlake; Plowboy Bend; Tuque Creek; Ray Carroll; Sugartree Bottoms
- 3 - FEDS: L385 (PIR Phase); Abilene ; Salina

Details on Remaining Breached Levees

See attached table, "Status of Construction Projects"

19 levees have remaining breaches to repair to restore levee to pre-2019 flood conditions

"Dirt is Moving" on at least 29 levees

Updated: 1 Jul 2020, previous report was 23 Jun 2020

The Kansas City District Corps of Engineers expects a two year duration for levee rehabilitation and does not expect to have levees repaired prior to spring 2020.

64 Levees approved for Repairs - repairs projects are now in Design and Construction Phase

1 Levee in Project Information Report / Damage Assessment Phase - if approved, these would move to Design and Construction Phase

6 Levee Repairs Advertised or Preparing to Award - levee repairs have been advertised for bidding and/or repair contracts are in process of being awarded

46 Levee Repairs Awarded under Contract - levee repairs have been awarded under new contracts or via modifications to existing contracts

Status of Levee Rehabilitation Requests for Assistance												
USACE / Sponsor Actions	USACE	USACE	Sponsor	USACE	USACE	USACE	USACE	Sponsor	Sponsor	Sponsor	USACE	USACE
Levee Unit/System	Project Information Report Approved by Northwestern Division	Engineering, Design, and Construction Funding Received	Borrow Identified	Project Cooperation Agreement Sent to Sponsor	Real Estate Easement Requirements Sent to Sponsor	Engineering and Design Plans and Specifications Drafted	Biddability, Constructability, Operability, Environmental, and Sustainability Review Certification	Project Cooperation Agreement Supplied to USACE	Real Estate Easement Requirements have been Acquired and Supplied to USACE	Cost Share or Work-in-Kind Received	Levee Repairs Advertised	Levee Repairs Awarded Under Contract
Count =	64	61	60	61	61	60	55	58	53	57	52	46
A-1 Levee District	X	NA	X	N/A	N/A	X	N/A	N/A	N/A	N/A	RFP	X
Bonne Femme Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Berger	X	X	X	N/A	N/A	X	N/A	N/A	N/A	N/A	RFP	X
Brunswick Levee District	X	X	X	X	X	X	X	X	Waiver	X	X	
Cambridge	X	X	X	X	N/A	X	N/A	Exhibit B	N/A	X	RFP	X
Canon Drainage District of Holt Co.	X	X	X	X	X	X	X	X	X	X	X	X
Capital View Levee	X	X	X	X	X	X	X	X	X	X	X	X
Cole Junction	X	X	X	X	X	X	X	X	X	X	X	X
Corning	X	X	X	X	X	X	X	X	X	X	X	X
Dewitt Section 2 & 1	X	X	X	X	X	X	X	X		X		
Garden of Eden Sec 2, & 3	X	X	X	X	X	X	X	X	X	X	X	X
Grape-Bollin -Schwartz (combined w/ Henry Pohl)	X	X	X	X	X	X	X	X	X	X	X	X
Hartsburg, Sec 1, 2, & 3	X	X	X	X	X	X	X	X	X	X	X	X
Henry Pohl (combined with Grape-Bollin-Sc)	X	X	X	X	X	X	X	X	X	X	X	X
Holt Co. No. 9	X	X	X	X	X			X				
Howard County LD No. 2	X	X	X	X	X	X	X	X	X	X	X	X
Howard County LD No. 4	X	X	X	X	X	X	X	X	X	X	X	X
Jacobs Levee	X	X	X	X	X	X	X	X	X	X	X	X
Kansas Department of Corrections	X	X	X	X	X	X	X	X	X	X	X	X
Labadie Section 5 & 6	X	X	X	Exhibit B	NA	X	N/A	Exhibit B	X	X	RFP	X
Levee District No. 1 of Cooper County	X	X	X	X	X	X	X	X	X	X	X	X
Malta Coles Saline-Lafayette Teteseau	X	X	X	X	X	X	X	X	X	X	X	X
Miami	X	X	X	X	X	X	X	X	X	X	X	X
Mi-De	X	X	X	X	X	X	X	X	X	X	X	X
MO Valley D&LD	X	X		X	X	X		X	X			
MO Valley Sections 1 and 2	X	X	X	X	X	X						
Mokane Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Morrison Lower Bottom	X	X	X	X	N/A	X	N/A	Exhibit B		X	RFP	X
NE Saline Levee Association	X	X	X	X	N/A	X	N/A	Exhibit B	N/A	X	RFP	X
Platte County Section 1, Rushville Sugarlake	X	X	X	X	X	X						
Platte County Section 2, Bean Lake	X	X	X	X	X	X	X	X	X	X	X	X
Plowboy Bend	X	X	X	X	X	X	X	X	X			
Ray Carroll	X											
Ray-Lafayette District & HCR	X	X	X	X	X	X	X	X	X	X	X	X

Non-Federal Levees (20% Sponsor Cost Share)

Status of Levee Rehabilitation Requests for Assistance												
USACE / Sponsor Actions	USACE	USACE	Sponsor	USACE	USACE	USACE	USACE	Sponsor	Sponsor	Sponsor	USACE	USACE
Levee Unit/System	Project Information Report Approved by Northwestern Division	Engineering, Design, and Construction Funding Received	Borrow Identified	Project Cooperation Agreement Sent to Sponsor	Real Estate Easement Requirements Sent to Sponsor	Engineering and Design Plans and Specifications Drafted	Biddability, Constructability, Operability, Environmental, and Sustainability Review Certification	Project Cooperation Agreement Supplied to USACE	Real Estate Easement Requirements have been Acquired and Supplied to USACE	Cost Share or Work-in-Kind Received	Levee Repairs Advertised	Levee Repairs Awarded Under Contract
Renz Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Reveaux Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Saline County Levee District No 2	X	X	X	X	X	X	X	X	X	X	X	X
Steedman Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Sugartree Levee District	X	X	X	X	N/A	X	N/A	Exhibit B		X		
Tebbetts Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Tri-County & Egypt	X	X	X	X	X	X	X	X	X	X	X	X
Tuque Creek Project	X	X	X	X	X	X	X					
Union Township	X	X	X	X	X	X	X	X	X	X	X	X
Holt Co. No. 10	X	X	X	X	X	X		X		X		
Wainwright Levee District	X	X	X	X	X	X	X	X	X	X	X	X
Wakenda	X	X	X	X	X	X	X	X	X	X	X	X
Whitham Drainage District, GOE Sec 1	X	X	X	X	X	X	X	X	X	X	X	X
Wolcott DD Section 1, 2, 3	X	X	X	X	X	X	X	X	X	X	X	X
North KC (2018)	X	X	X	X	X	X	X	X	X	NA	X	X
246-L (2018 & 2019)	X	X	X	X	X	X	X	X	X	NA	X	
500-R	X	X	X	X	X	X	X	X	X	NA	X	
Kimsey-Holley	X	X	X	X	X	X	X	X	X	NA	X	X
497-L	X	X	X	X	X	X	X	X	X	NA	X	X
488-L	X	X	X	X	X	X	X	X	X	NA	X	X
455-L	X	X	X	X	X	X	X	X	X	NA	X	X
448-443-L	X	X	X	X	X	X	X	X	X	NA	X	X
471-460-R	X	X	X	X	X	X	X	X	X	NA	X	X
440-R	X	X	X	X	X	X	X	X	X	NA	X	X
408-L	X	X	X	X	X	X	X	X	X	NA	X	X
400-L	X	X	X	X	X	X	X	X	X	NA	X	X
385-L												
Lower Chariton	X	X	X	X	X	X		X	Waiver	NA	X	
East Bottoms	X	X	X	X	X	X	X	X	X	NA	X	X
Abilene, KS	X									NA		
Salina	X									NA		

Federal Levees (100% Federal Costs)

****Blue Highlighted cells show project progress since previous report dated 23 Jun 2020**

***Withdrawn (West Glasgow, McBaine, Big Bend, Linneman-Weekley) and Ineligible (Chamois, 476, 482, North KC 2019, South Topeka, Soldier Creek, North Topeka, CID-MO, CID-KS, Argentine, Armourdale, 351-R) requests have been removed

Process Step Definitions
Project Information Report Approved by Northwestern Division - Project Information Report has been reviewed and approved based upon the recommended repairs, alternatives considered, environmental considerations, and the benefit-to-cost-ratio.
Engineering, Design, and Construction Funding Received - Federal funding has been provided to Kansas City District for the repairs to be designed and constructed
Borrow Identified - A sufficient quantity of acceptable borrow material has been identified to support the required repairs.
Project Cooperation Agreement Sent to Sponsor - USACE has provided two copies of the cooperation agreement and supporting exhibits to the sponsor defining the sponsor's legal obligation to complete the construction project.
Real Estate Easement Requirements Sent to Sponsor - permanent easement requirements for new features and temporary easement requirements for borrow and construction limits have been documented and provided to the sponsor.
Engineering and Design Plans and Specifications Drafted -The concept repair drawings from the PIR have been modified into contract documents (plans and the specifications) that are ready for review.
Biddability, Constructability, Operability, Environmental, and Sustainability Review Certification - A review conducted on the draft plans and specifications to ensure the design meets the requirements for biddability, constructability, operability, environmental, and sustainability.
Project Cooperation Agreement Supplied to USACE - The sponsor has provided a signed copy of the project cooperation agreement along with all other supporting documentation.
Real Estate Easement Requirements have been Acquired and Supplied to USACE - The sponsor has certified they have acquired all real estate to support the repairs and construction activities.
Cost Share or Work-in-Kind Received - The sponsor has provided their share of the appropriate cost share in cash, an agreement to complete work-in-kind, or a combination of the two to fully support the project cost share requirement.
Contract Advertised -The contract has been publicly advertised for prospective bidders to provide a qualified bid to construct the project. Contracts can not be advertised until funding, real estate certification, and Project Cooperation Agreements are provided to the Kansas City
Contract Awarded - The winning bidder has been validated, contract has been awarded, and funds have been obligated for payment.

Status of Levee Rehabilitation Construction Contracts

Updated: 1 Jul 2020, previous report was 23 Jun 2020

Contract Number	Resident Office	Levee Unit/System	County	State	Damage Type (Breach, Scour, Underseepage, Levee Slope Slides, Overtopping Damage, Grass Kill)	Bid Opening Date	Contract Amount	Construction Contractor	Contract Award Date (CC800)	Notice to Proceed Date (CW440)	Contract Required Completion (CC830)	% Complete USACE Construction Contract	Level of Protection in Place?
W912DQ20C1081	LVN	Canon Drainage District of Holt Co.	Holt	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	6/8/2020	\$726,392	Circle V Harvesting	6/19/2020	7/03/2020 (PROJECTED)	12/30/2020 (PROJECTED)	NTP not yet issued	
Contract not awarded	LVN	Corning	Holt	MO	Breach, Crown Erosion, Slope Slides, Scour, Grass Kill	7/10/2020			7/24/2020 (PROJECTED)			Not awarded	
Contract not advertised	LVN	Holt Co. No. 9	Holt	MO	Breach, Underseepage, Overtopping, Levee Slope Slides, Scour, Grass Kill	TBD			TBD			Not awarded	
W912DQ20C1086	LVN	Union Township	Holt	MO	Breaches, Overtopping, Levee Slope Slides, Grass Kill	6/12/2020	\$411,357	Barnes Area Services	7/1/2020	7/15/2020 (PROJECTED)	12/12/2020 (PROJECTED)	NTP not yet issued	
Contract not advertised	LVN	Holt Co. No. 10	Holt	MO	Breaches, Overtopping, Levee Slope Slides, Grass Kill	TBD			TBD			Not awarded	
W912DQ20C1011	LVN	Kansas Department of Corrections	Leavenworth	KS	Breach, Overtopping, Levee Slope Slides, Grass Kill	2/6/2020	\$626,000	Medvolt	3/12/2020	3/19/2020	9/15/2020	64%	
W912DQ20C1022	LVN	Grape-Bollin -Schwartz	Atchison, Leavenworth	KS	Breach, Overtopping, Levee Slope Slides	1/29/2020	\$191,757	King's Construction	3/13/2020	4/8/2020	10/5/2020	33%	
W912DQ20C1022	LVN	Henry Pohl	Atchison	KS	Breach, Overtopping, Levee Slope Slides, Scour	1/29/2020	\$149,798	King's Construction	3/13/2020	4/8/2020	10/5/2020	99%	
W912DQ20C1053	LVN	Wolcott DD Section 1, 2, 3	Wyandotte, Leavenworth	KS	Breach, Overtopping, Levee Slope Slides, Grass Kill	3/25/2020	\$624,000	Medvolt	4/9/2020	5/4/2020	10/31/2020	0%	
Contract not advertised	KCL	Plowboy Bend	Moniteau	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	TBD			TBD			Not awarded	Yes
W912DQ20C1023	KCL	Wainwright Levee District	Callaway	MO	Overtopping, Levee Slope Slides, Underseepage, Ramp Erosion, Damaged Drainage Structure, Grass Kill	2/27/2020	\$99,787	Dogwood	3/19/2020	4/16/2020	8/14/2020	65%	Yes
W912DQ20C1030	KCL	Capital View Levee	Callaway	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	3/12/2020	\$267,354	Remsel Corp	3/30/2020	4/20/2020	9/17/2020	75%	Yes
W912DQ20C1031	KCL	Howard County LD No. 4	Howard	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	3/12/2020	\$296,500	Academy Consulting	3/26/2020	4/13/2020	10/10/2020	15%	Yes
W912DQ20C1032	KCL	Hartsburg, Sec 1, 2, & 3	Boone	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	3/16/2020	\$290,148	Carl L Jones	3/30/2020	4/13/2020	10/10/2020	Sect 1-100%, Sect 2-100% Sect 3 60%	Yes
W912DQ20C1033	KCL	Jacobs Levee	Callaway	MO	Levee Slope Slides, Overtopping, Grass Kill	3/13/2020	\$24,913	Dogwood	3/25/2020	4/13/2020	8/11/2020	100%	Yes
W912DQ20C1033	KCL	Tebbetts Levee District	Callaway	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	3/12/2020	\$63,610	Dogwood	3/25/2020	4/13/2020	8/11/2020	80%	Yes
W912DQ20C1034	KCL	Levee District No. 1 of Cooper County	Cooper, Moniteau	MO	Breach, Levee Slope Slides, Underseepage, Grass Kill	3/20/2020	\$174,640	Carl L Jones	3/31/2020	4/10/2020	9/7/2020	15%	Yes
W912DQ20C1040	KCL	Mokane Levee District	Callaway	MO	Overtopping, Foreshore Erosion, Grass Kill	3/16/2020	\$111,313	Dogwood	3/30/2020	4/14/2020	9/11/2020	10%	Yes
W912DQ20C1046	KCL	Cole Junction	Cole	MO	Grass Kill	3/13/2020	\$34,260	Greis Trucking and Excavating	3/29/2020	4/13/2020	9/10/2020	100%	Yes
W912DQ20C1054	KCL	FCCE 2019 NF Howard County LD No. 2 and LD No. 3, Sec 1 & 2, No. 7 Sec 4	Howard	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	3/20/2020	\$216,150	R&L Boone	4/1/2020	4/13/2020	10/10/2020	Howard 2-100%, Howard 3-90%, Howard 7-75%	Yes
W912DQ20C1063	KCL	Renz Levee District	Callaway	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	4/19/2020	\$72,483	Dogwood	4/14/2020	4/24/2020	8/22/2020	30%	Yes
W912DQ20C1066	KCL	440-R	Atchison, Doniphan	KS	Underseepage	4/9/2020	\$333,960	AIM Services, LL	4/22/2020	5/26/2020	9/18/2020	5%	Yes
W912DQ20C1067	KCL	408-L	Platte	MO	Scour, Levee Slope Slide, Underseepage	4/7/2020	\$337,024	HB Construction	5/7/2020	5/18/2020	9/27/2020	5%	Yes
W912DQ20C1067	KCL	400-L	Platte	MO	Scour, Underseepage	4/7/2020	\$364,613	HB Construction	5/7/2020	5/18/2020	9/27/2020	5%	Yes

Status of Levee Rehabilitation Construction Contracts

Updated: 1 Jul 2020, previous report was 23 Jun 2020

Contract Number	Resident Office	Levee Unit/System	County	State	Damage Type (Breach, Scour, Underseepage, Levee Slope Slides, Overtopping Damage, Grass Kill)	Bid Opening Date	Contract Amount	Construction Contractor	Contract Award Date (CC800)	Notice to Proceed Date (CW440)	Contract Required Completion (CC830)	% Complete USACE Construction Contract	Level of Protection in Place?
W912DQ18D1000 W912DQ20F0011	ROKC	East Bottoms	Jackson	MO	Scour	1/29/2020	\$3,331,200	Ellis	2/21/2020	3/13/2020	12/8/2020	100%	Yes
W912DQ20C1007	ROKC	North KC (2018)	Clay	MO	Erosion, Pump Damage	11/13/2019	\$226,925	ESI	12/3/2019	1/16/2020	10/22/2020	100%	Yes
W912DQ20C1009	ROKC	471-460-R	Doniphan, Buchanan	KS, MO	Levee Slope Slides, Underseepage, Grass Kill	12/13/2020	\$138,000	MCON	1/24/2020	4/9/2020	8/7/2020	0%	Yes
W912DQ20C1075	ROKC	Platte County Section 2, Bean Lake	Platte	MO	Breach, Overtopping, Levee Slope Slides, Scour, Rail Erosion, Grass Kill		\$336,631	HB Construction	5/29/2020	6/12/2020 (PROJECTED)	12/9/2020 (PROJECTED)	NTP not yet issued	
Contract not awarded	ROKC	246-L	Chariton	MO	Breach, Scour, Underseepage, Levee Slope Slides, Overtopping Damage, Grass Kill	6/23/2020			6/25/2020 (PROJECTED)			Not awarded	
Contract not awarded	ROKC	500-R	White Cloud	KS	Breach, Scour, Underseepage, Overtopping Damage, Grass Kill	7/1/2020			7/15/2020 (PROJECTED)			Not awarded	
W912DQ20C1074	ROKC	Kimsey-Holley	Holt	MO	Erosion, Grass Kill	5/7/2020	\$585,000	Fenton	6/12/2020	7/2/2020 (PROJECTED)	12/23/2021 (PROJECTED)	NTP not yet issued	Yes
W912DQ20C1074	ROKC	497-L	Holt	MO	Scour, Underseepage, Grass Kill	5/7/2020	\$920,000	Fenton	6/12/2020	7/2/2020 (PROJECTED)	12/23/2021 (PROJECTED)	NTP not yet issued	Yes
W912DQ20C1074	ROKC	488-L	Holt	MO	Scour, Grass Kill	5/7/2020	\$328,000	Fenton	6/12/2020	7/2/2020 (PROJECTED)	12/23/2021 (PROJECTED)	NTP not yet issued	Yes
W912DQ20C1074	ROKC	455-L	Buchanan	MO	Levee Slope Slides, Underseepage, Scour, Grass Kill	5/7/2020	\$77,830	Fenton	6/12/2020	7/2/2020 (PROJECTED)	12/23/2021 (PROJECTED)	NTP not yet issued	Yes
W912DQ20C1074	ROKC	448-443-L	Buchanan	MO	Underseepage, Grass Kill	5/7/2020	\$32,200	Fenton	6/12/2020	7/2/2020 (PROJECTED)	12/23/2021 (PROJECTED)	NTP not yet issued	Yes
Contract not awarded	ROKC	Lower Chariton	Chariton	MO	Scour, Underseepage, Levee Slope Slides, Grass Kill	7/21/2020			8/4/2020 (PROJECTED)			Not awarded	Yes
Contract not advertised	ROKC	Platte County Section 1, Rushville Sugarlake	Platte	MO	Breach, Overtopping, Levee Slope Slides	TBD			TBD			Not awarded	
W912DQ20C1073	LCAAP	Wakenda	Carroll	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	5/7/2020	\$124,750	Jacob Smith	5/18/2020	6/1/2020 (PROJECTED)	10/29/2020 (PROJECTED)	0%	Yes
W912DQ20C1077	LCAAP	Malta Coles Saline-Lafayette Teteseau	Saline	MO	Overtopping, Levee Slope Slides, Underseepage, Grass Kill	5/11/2020	\$229,493	Circle V Harvesting	5/29/2020	6/11/2020	12/8/2020	0%	
Contract not advertised	LCAAP	Ray Carroll	Ray	MO	Breaches, Underseepage, Levee Slope Slides, Scour, Grass Kill, Damage Drainage Structure	TBD			TBD			Not awarded	Yes
W912DQ18C1049	OFM-O	A-1 Levee District	Osage, Gasconade	MO	Levee Slope Slides, Overtopping, Grass Kill	N/A	\$98,000	C.L. Richardson Construction	6/8/2018	8/8/2018	11/2/2020	32%	Yes
W912DQ18C1049	OFM-O	Morrison Lower Bottom	Gasconade	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	N/A	\$57,000	C.L. Richardson Construction	6/8/2018	8/8/2018	11/2/2020	32%	Yes
W912DQ18C1055	OFM-O	Labadie Section 4, 5 & 6	Franklin	MO	Breach, Overtopping	N/A	\$238,000	Circle V Harvesting	1/30/2020	1/31/2020	9/30/2020	4-100%, 5-0%, 6-0%	Yes
W912DQ18C1066	OFM-O	Cambridge	Saline	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	N/A	\$550,062	TriSmith	3/20/2020	3/20/2020	8/30/2020	90%	Yes
W912DQ18C1066	OFM-O	NE Saline Levee Association	Saline	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	N/A	\$758,117	TriSmith	3/20/2020	3/20/2020	8/30/2020	80%	Yes
W912DQ18C1067	OFM-O	Berger	Franklin	MO	Levee Slope Slides, Grass Kill	N/A	\$29,800	Klocke, Inc	1/28/2020	1/29/2020	9/30/2020	0%	Yes
W912DQ20C1010	OFM-O	Mi-De	Carroll	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	1/29/2020	\$217,227	CC Schlueter, Inc	2/10/2020	2/28/2020	8/26/2020	99%	Yes
W912DQ20C1029	OFM-O	Garden of Eden Sec 2, & 3	Chariton	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	3/10/2020	\$437,813	C C Schluter Inc	3/26/2020	4/13/2020	12/9/2020	Sect 2-80%, Sect 3-0%	
W912DQ20C1035	OFM-O	Whitham Drainage District, GOE Sec 1	Chariton	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	3/6/2020	\$774,303	Better by Design	3/28/2020	4/20/2020	11/6/2020	50%	

Status of Levee Rehabilitation Construction Contracts													
Updated: 1 Jul 2020, previous report was 23 Jun 2020													
Contract Number	Resident Office	Levee Unit/System	County	State	Damage Type (Breach, Scour, Underseepage, Levee Slope Slides, Overtopping Damage, Grass Kill)	Bid Opening Date	Contract Amount	Construction Contractor	Contract Award Date (CC800)	Notice to Proceed Date (CW440)	Contract Required Completion (CC830)	% Complete USACE Construction Contract	Level of Protection in Place?
W912DQ20C1052	OFM-O	Steedman Levee District	Callaway	MO	Breach, Overtopping, Levee Slope Slides, Gravel Washout, Grass Kill	3/17/2020	\$165,000	Greis Trucking and Excavating	3/31/2020	4/20/2020	9/17/2020	90%	Yes
W912DQ20C1061	OFM-O	Ray-Lafayette District & HCR	Ray	MO	Levee Slope Slides, Grass Kill	4/7/2020	\$146,299	Circle V Harvesting	4/29/2020	5/18/2020	10/15/2020	0%	Yes
W912DQ20C1071	OFM-O	Tri-County & Egypt	Clay, Ray	MO	Breach, Overtopping, Underseepage, Levee Slope Erosion, Grass Kill	4/30/2020	\$146,299	Padgett Brothers Excavating	5/8/2020	6/1/2020	9/29/2020	0%	Yes
W912DQ20C1072	OFM-O	Bonne Femme Levee District	Howard	MO	Breaches, Levee Slope Slides, Scour, Grass Kill	5/1/2020	\$135,000	Greis Trucking and Excavating	5/5/2020	6/1/2020	10/29/2020	0%	Yes
W912DQ20C1079	OFM-O	Saline County Levee District No 2	Saline	MO	Breach, Overtopping, Levee Slope Slides, Foreshore Erosion, Scour, Grass Kill	5/20/2020	\$493,411	Academy Consulting	5/29/2020	6/16/2020	1/12/2020	0%	
W912DQ20C1082	OFM-O	Miami	Saline	MO	Levee Slope Slides, Grass Kill	6/9/2020	\$59,719.00	Jacob Smith	6/18/2020	7/2/2020 (PROJECTED)	11/29/2020 (PROJECTED)	NTP not yet issued	Yes
Contract not awarded	OFM-O	Brunswick Levee District	Carroll	MO	Breach, Overtopping, Levee Slope Slides, Scour, Grass Kill	7/15/2020			7/29/2020 (PROJECTED)			Not awarded	
Contract not advertised	OFM-O	Sugartree Levee District	Carroll	MO	Overtopping, Underseepage, Levee Slope Erosion, Grass Kill	Overdue		BHE, LLC	5/4/2018	6/22/2018	10/30/2020	75%	Yes
Contract not advertised	OFM-O	Dewitt Section 2 & 1	Carroll	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	TBD			TBD			Not awarded	Yes
Contract not advertised	OFM-O	MO Valley D&LD	Warren	MO	Levee Slope Slides, Grass Kill	TBD			TBD			Not awarded	Yes
Contract not advertised	OFM-O	MO Valley Sections 1 and 2	Warren	MO	Underseepage, Foreshore Erosion	TBD			TBD			Not awarded	Yes
Contract not awarded	OFM-O	Reveaux Levee District	Callaway	MO	Breach, Overtopping, Levee Slope Slides, Grass Kill	7/10/2020			7/25/2020 (PROJECTED)			Not awarded	
Contract not advertised	OFM-O	Tuque Creek Project	Warren	MO	Breach, Overtopping, Levee Slope Erosion, Foreshore Erosion, Grass Kill	TBD			TBD			Not awarded	Yes
Contract not advertised	Riley	Abilene, KS	Dickinson	KS	Scour	TBD			TBD			Not awarded	Yes
Contract not advertised	Riley	Salina, KS	Saline	KS	Scour	TBD			TBD			Not awarded	Yes
PIR Phase	TBD	385-L	Platte	MO	Channel erosion	TBD			TBD			Not awarded	Yes

Process Step Definitions:

Contract Award occurs when all pre-award contractor bonds have been reviewed to ensure the contractor has the ability to complete the work.

Notice to Proceed is the official start of the contract period and allows the contractor to begin construction work.

Level of Protection In Place means all breaches are closed or the levee was not breached during flooding and the levee has been repaired to approximately the pre-flood

Levee Repairs Complete means all repairs covered under the contract have been completed. Sponsors may be responsible for completing additional repairs.
